



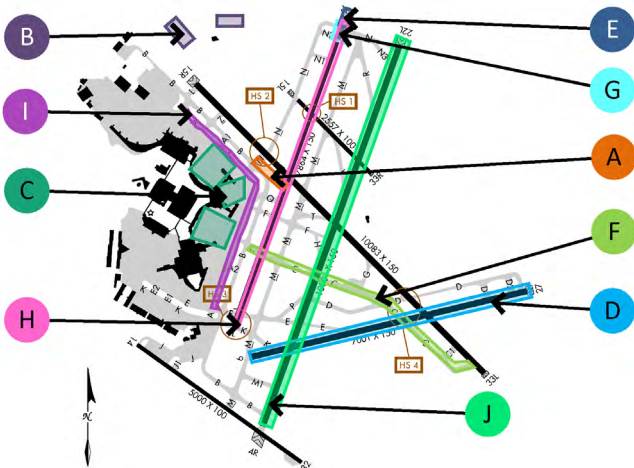

		2026										2027												2028												2029		
	Project	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	
D	RWY 27 RSA (Phase 2)					R	R	R	R																													
E	RWY 22R Approach										Y	Y	Y	Y	Y	Y	Y	Y	Y	Y	Y	Y																

	Project	Description of Work	Estimated Dates	Status	Impact	Notes
D	RWY 27 RSA (Phase 2)	Phase 2 of the 27 RSA project. Requires additional 75-day closure. Construction of RWY 27 safety area on a pile supported deck continued from 2025 Phase 1.	08/31/2026 to 11/15/2026	Upcoming	R	This is Phase 2 of the RWY 9 EMAS installation and requires a continuous closure of Runway 9/27 for approximately 75 days. The loss of RWY 9/27 will impact the airport capacity. Configurations requiring RWY 9/27 will not be available. With the loss of RWY 9 for departures, NE Flow AAR's are as follows: VMC Arrival 4L/4R and Depart 4R: AAR 42, VMC/LVMC Arrival 4L and Depart 4R: AAR 34, and IMC (with 4L RNAV minimums) Land 4L and Depart 4R: AAR 32. Arrive and Depart 4R IMC rate unchanged. Rates may fluctuate based on arrival/departure demand. Facility expects GDPs, GS, MIT throughout the project. Pending FAA SRM/Massport Final Approval- RWY 27 might be available for departure only from TWY D2 from approximately 9/7 through 10/31.
E	RWY 22R Approach	Small portion of RWY 22R pavement to be rehabilitated.	2027 TBD	Upcoming	Y	Project was pushed back to integrate into the RWY 4L-22R rehab planned in 2027. Impact only occurs when weather forces NE or SW configuration.

IATA Level 2

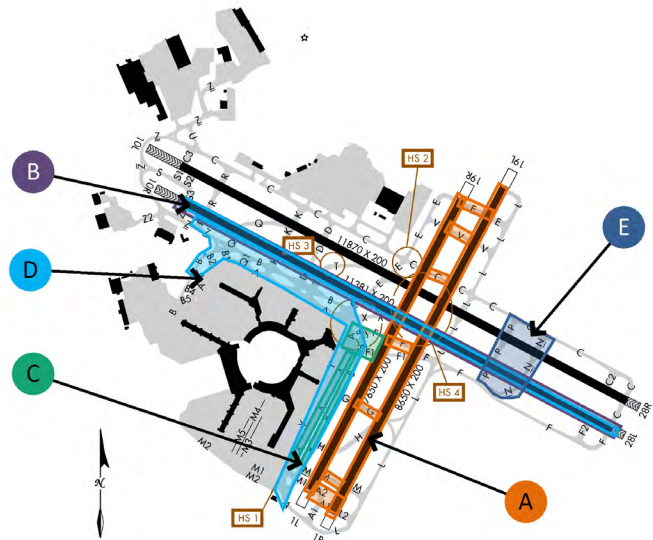

		2026										2027												2028												2029		
	Project	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	
A	RWY 1R/19L Rehabilitation and TWY W	Y	Y	Y	Y	Y	Y	Y	Y	G																												
B	RWY 10R/28L Lighting										G	G	G	G	G	G	G	G	G	G	G	G																

	Project	Description of Work	Estimated Dates	Status	Impact	Notes
A	RWY 1R/19L Rehabilitation and TWY W	Phase 1: Repaving runway and upgrading associated infrastructure. Demolishing TWY F1 and constructing TWY W. Realign TWY F to the south 50 feet. Both RWYs 1R/19L and 1L/19R closed for rehabilitation. TWYs E, V, C, F, F1, G, H, M, A1, A2 closed for rehabilitation for repaving between RWYs 1L and 1R. EMAS seam replacement. Replace navigational lighting and signage.	03/30/2026 to 10/03/2026	In Progress	Y	Both RWY 1L/19R and 1R/19L will be closed for 6 months.
		Phase 2: Repaving TWY F and TWY L intersection.	10/12/2026 to 11/14/2026	Upcoming	G	Increase taxi time for 28s Departures. All four runways open for use.
B	RWY 10R/28L Lighting	RWY 10R/28L closed for new lighting cable.	2027 TBD	Upcoming	G	No RWY 28L closure as of last briefing
